SEWER JUNCTION INFORMATION FROM SEWER VIDEO INSPECTION SEWER ID S-MA20016529		
DISTANCE FROM MH ID S-MH20015017		
DISTANCE	DIAMETER	CLOCK
3.20	150	10
4.50	150	2
11.30	150	10
19.20	150	2
21.10	150	10
23.60	150	2
26.60	150	12
26.60	150	2
29.60	150	10
37.10	150	2
38.40	150	10
47.60	150	2
48.10	150	10
58.00	150	10
58.00	150	1
62.00	150	2
75.60	150	10
78.10	150	2
84.20	150	10
88.40	150	2
90.90	150	10
94.00	150	10
97.60	150	2

MARYLAND STREET

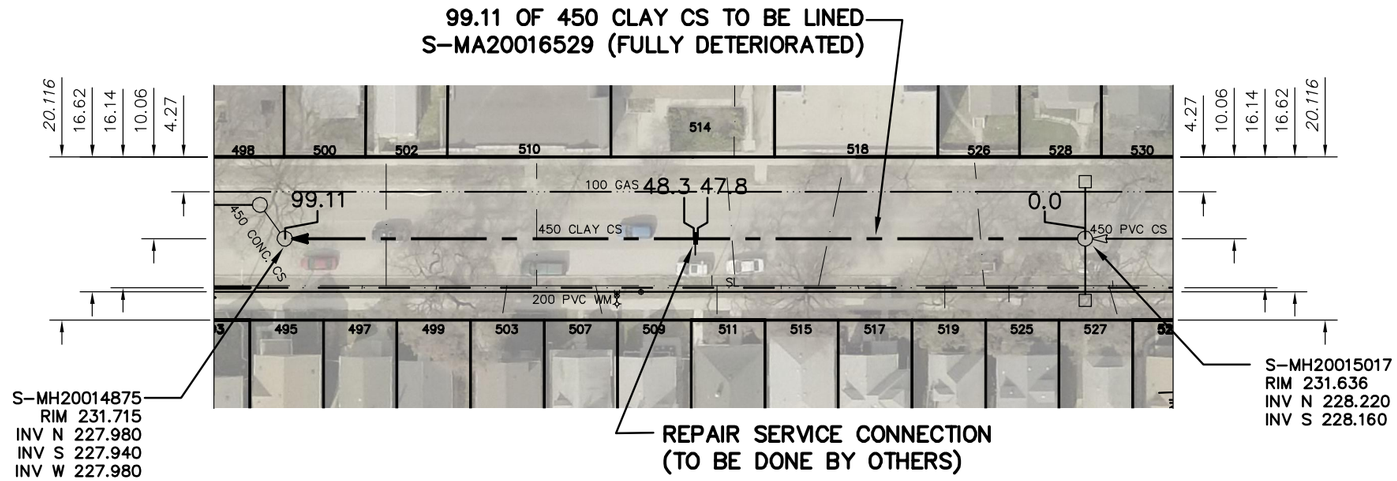

WARNING

IF POWER EQUIPMENT OR EXPLOSIVES ARE TO BE USED FOR EXCAVATION ON THIS PROJECT THE CONTRACTOR MUST:

1) NOTIFY THE GAS COMPANY OF THE PROPOSED LOCATION OF EXCAVATION.

2) TAKE PRECAUTION TO AVOID DAMAGE TO GAS COMPANY INSTALLATIONS.

SEE PROVINCIAL REGULATION 210/72 FOR DETAILS

FOR INDEX SEE 11020

METRIC
WHOLE NUMBERS INDICATE MILLIMETRES
DECIMALIZED NUMBERS INDICATE METRES
0.0 10.0 20.0 30.0 40.0

LOCATION APPROVED
UNDERGROUND STRUCTURES

SUPV. U/G STRUCTURES COMMITTEE — DATE

NOTE:

LOCATION OF UNDERGROUND STRUCTURES AS SHOWN ARE BASED ON THE BEST INFORMATION AVAILABLE BUT NO GUARANTEE IS GIVEN THAT ALL EXISTING UTILITIES ARE SHOWN OR THAT THE GIVEN LOCATIONS ARE EXACT. CONFIRMATION OF EXISTENCE AND EXACT LOCATION OF ALL SERVICES MUST BE OBTAINED FROM THE INDIVIDUAL UTILITIES BEFORE PROCEEDING WITH CONSTRUCTION.

B.M.
ELEV.

COSTRUCTION COMPLETION DATE: YYYY MM DD

NO.	REVISIONS	DATE	BY

DESIGNED BY	NC	CHECKED BY	SC
DRAWN BY	CN	APPROVED BY	KZ
SCALE: HORIZONTAL	1:750	RELEASED FOR CONSTRUCTION	KAS ZUREK
VERTICAL			
DATE	2016 01 29	DATE	

PLOT DATE: 2016 01 29

ENGINEER'S SEAL
ORIGINAL SIGNED BY N.M. CONTI 16/01/28

CONSULTANT DRAWING NUMBER
–

Winnipeg

THE CITY OF WINNIPEG
WATER AND WASTE DEPARTMENT
ENGINEERING DIVISION

2015 SEWER RENEWALS
BY CIPP LINING

MARYLAND STREET

2ND MH N ELLICE AVENUE TO
1ST MH N ELLICE AVENUE

SHEET 29 OF 56

CITY DRAWING NUMBER
11046

BID OPPORTUNITY: 960-2015
CONTRACT NUMBER: 1

FILE PATH: R:\DRAWINGS\SEWER\2015 RENEWALS\RENEWALS & ASSOSTIATED WORKS\Contract 1\Construction Dwg\
FILE NAME: MARYLAND S-MA20016529.dwg
